Analyse de Sinchro

Projet Erasmus+ Climatelabs | 2020 - 2023


1 Objectif:

Cette document est une anlyse globale de l'outil Sinchro pour le Projet Climatelabs piloté au sein de l'ENSGSI

1.1 Temps estimé selon le Grant Agreement du projet

1.1.1 Gantt Original de Climatelabs

Planning ClimateLabs



Last Updated : 28 September, 2022

1.1.2 Quantité de jours per WP initial

WP	Role	Coût de chaque Rôle (Euros/Jour)	Jours (G.A.)
Preparation	Manager	280	0
Preparation	EC/Enseignant	214	16
Preparation	Technicien	162	9
Preparation	Administratif	131	0
Development	Manager	280	6
Development	EC/Enseignant	214	47
Development	Technicien	162	35
Development	Administratif	131	0
Quality Plan	Manager	280	2
Quality Plan	EC/Enseignant	214	5
Quality Plan	Technicien	162	0
Quality Plan	Administratif	131	0
Dissemination exploitation	Manager	280	1
Dissemination exploitation	EC/Enseignant	214	19
Dissemination exploitation	Technicien	162	2
Dissemination exploitation	Administratif	131	0
Management	Manager	280	2
Management	EC/Enseignant	214	8
Management	Technicien	162	10
Management	Administratif	131	10

2 Total of days

Role	Days
Administratif	10
EC/Enseignant	95
Manager	11
Technicien	56

3 UL Sinchro: Janvier 2020 - oct 25 2023

Task	Role	CLAUDINE	FABIO	FERNEY	LAU
WP 1.1 : Changemaker	EC/Enseignant	3.0	18.25		
WP 1.1 : Changemaker	Technicien		1.75	6.00	
WP1.2 : Kick-?Off	EC/Enseignant		4.50		
WP1.2 : Kick-?Off	Technicien		0.75	1.00	
WP1.3 : External	EC/Enseignant				
WP1.3 : External	Technicien				
WP2.1: Social	EC/Enseignant				
WP2.1: Social	Manager				
WP2.1: Social	Technicien				
WP2.2 : Design and Development	EC/Enseignant	7.0	18.75		
WP2.2 : Design and Development	Manager		4.00		
WP2.2 : Design and Development	Technicien			32.00	
WP2.4 : Applied Research Pilot	EC/Enseignant		1.00	1.50	
WP2.4 : Applied Research Pilot	Manager		1.00		
WP2.4 : Applied Research Pilot	Technicien			4.00	
	WP 1.1 : Changemaker WP 1.1 : Changemaker WP1.2 : Kick-?Off WP1.2 : Kick-?Off WP1.3 : External WP1.3 : External WP2.1 : Social WP2.1 : Social WP2.1 : Social WP2.2 : Design and Development WP2.2 : Design and Development WP2.2 : Design and Development WP2.4 : Applied Research Pilot WP2.4 : Applied Research Pilot	WP 1.1 : Changemaker WP 1.1 : Changemaker Technicien WP1.2 : Kick-?Off WP1.2 : Kick-?Off Technicien WP1.3 : External WP1.3 : External Technicien WP2.1 : Social WP2.1 : Social WP2.1 : Social WP2.2 : Design and Development WP2.2 : Design and Development WP2.2 : Design and Development WP2.4 : Applied Research Pilot WP2.4 : Applied Research Pilot Mennicien EC/Enseignant Manager Technicien EC/Enseignant Manager Technicien EC/Enseignant Manager Technicien EC/Enseignant Manager	WP 1.1 : Changemaker WP 1.1 : Changemaker Technicien WP1.2 : Kick-?Off EC/Enseignant WP1.3 : External WP1.3 : External WP2.1 : Social WP2.1 : Social WP2.1 : Social WP2.2 : Design and Development WP2.2 : Design and Development WP2.2 : Design and Development WP2.3 : Applied Research Pilot WP2.4 : Applied Research Pilot Manager WP2.4 : Applied Research Pilot Manager 3.0 3.0 3.0 3.0 3.0 3.0 3.0 3.0 3.0 3.	WP 1.1 : Changemaker EC/Enseignant 3.0 18.25 WP 1.1 : Changemaker Technicien 1.75 WP 1.2 : Kick-?Off EC/Enseignant 4.50 WP 1.3 : External EC/Enseignant Technicien 0.75 WP 1.3 : External EC/Enseignant Technicien WP 2.1 : Social EC/Enseignant WP 2.1 : Social Manager WP 2.1 : Social Technicien WP 2.2 : Design and Development EC/Enseignant 7.0 18.75 WP 2.2 : Design and Development Manager 4.00 WP 2.3 : Applied Research Pilot EC/Enseignant 1.00 WP 2.4 : Applied Research Pilot Manager 1.00	WP 1.1 : Changemaker EC/Enseignant 3.0 18.25 WP 1.1 : Changemaker Technicien 1.75 6.00 WP1.2 : Kick-?Off EC/Enseignant 4.50 WP1.2 : Kick-?Off Technicien 0.75 1.00 WP1.3 : External EC/Enseignant WP2.1 : Social EC/Enseignant WP2.1 : Social Manager WP2.1 : Social Technicien WP2.2 : Design and Development EC/Enseignant 7.0 18.75 WP2.2 : Design and Development Manager 4.00 WP2.2 : Design and Development Technicien 32.00 WP2.4 : Applied Research Pilot EC/Enseignant 1.00 1.50 WP2.4 : Applied Research Pilot Manager 1.00 1.50

WP	Task	Role	CLAUDINE	FABIO	FERNEY	LAU
Quality Plan	WP3 : Quality monitoring and E	EC/Enseignant		4.00	1.00	
Quality Plan	WP3: Quality monitoring and E	Manager		1.50		
Dissemination exploitation	WP4.1 : Dissemination plan def	EC/Enseignant				
Dissemination exploitation	WP4.1 : Dissemination plan def	Manager				
Dissemination exploitation	WP4.1 : Dissemination plan def	Technicien				
Dissemination exploitation	WP4.2 : Latin American Applied	EC/Enseignant				
Dissemination exploitation	WP4.2 : Latin American Applied	Manager				
Dissemination exploitation	WP4.2 : Latin American Applied	Technicien				
Dissemination exploitation	WP4.3 : Outreach	EC/Enseignant	2.5	5.25		
Dissemination exploitation	WP4.3 : Outreach	Manager		3.50		
Dissemination exploitation	WP4.3 : Outreach	Technicien			2.00	
Dissemination exploitation	WP4.4 : Design and Content Edi	EC/Enseignant		1.50		
Dissemination exploitation	WP4.4: Design and Content Edi	Manager		1.00		
Dissemination exploitation	WP4.4: Design and Content Edi	Technicien			1.00	
Management	WP5: Management and coordinat	EC/Enseignant	2.0	6.00		
Management	WP5: Management and coordinat	Manager		3.00		
Management	WP5: Management and coordinat	Technicien		1.00	13.25	
Management	WP5 : Management and coordinat	Administratif		0.50	11.00	

3


4 Sinchro UL - ClimateLabs

WP	Role	Jours.GA	Sincro.UL
Preparation	Manager	0	
Preparation	EC/Enseignant	16	44.75
Preparation	Technicien	9	9.50
Preparation	Administratif	0	
Development	Manager	6	6.00
Development	EC/Enseignant	47	48.50
Development	Technicien	35	36.00
Development	Administratif	0	
Quality Plan	Manager	2	2.50
Quality Plan	EC/Enseignant	5	5.00
Quality Plan	Technicien	0	
Quality Plan	Administratif	0	
Dissemination exploitation	Manager	1	5.50
Dissemination exploitation	EC/Enseignant	19	21.00
Dissemination exploitation	Technicien	2	3.00
Dissemination exploitation	Administratif	0	
Management	Manager	2	3.00
Management	EC/Enseignant	8	10.00
Management	Technicien	10	14.25
Management	Administratif	10	11.50

Role	Days	Days_UL	Days_to_declare
Administratif	10	11.50	-1.50
EC/Enseignant	95	129.25	-34.25
Manager	11	17.00	-6.00

Role	Days	Days_UL	Days_to_declare
Technicien	56	62.75	-6.75

Graph

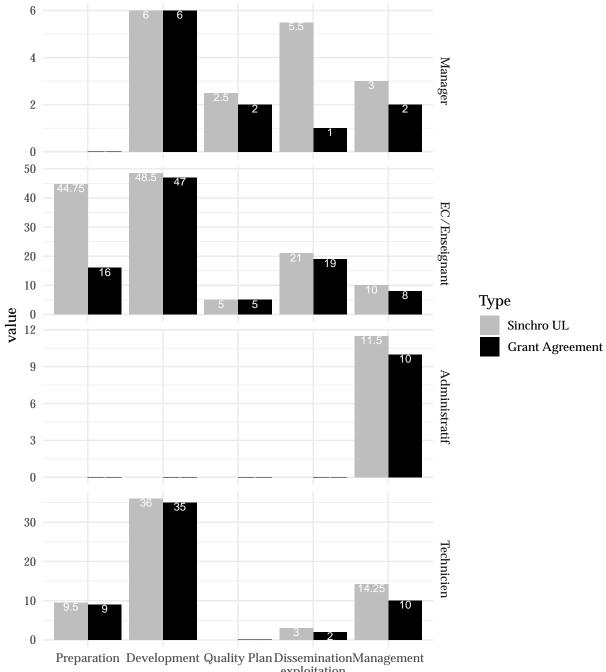

 $\begin{array}{c} Preparation \ \ Development \ Quality \ Plan \ Dissemination Management \\ exploitation \end{array}$ WP

Sinchro: Janvier 2020 - oct 25 2023
